Sherborn Library Project

Sherborn, MA

- **LBC Progress Update**
- **September 8, 2021**

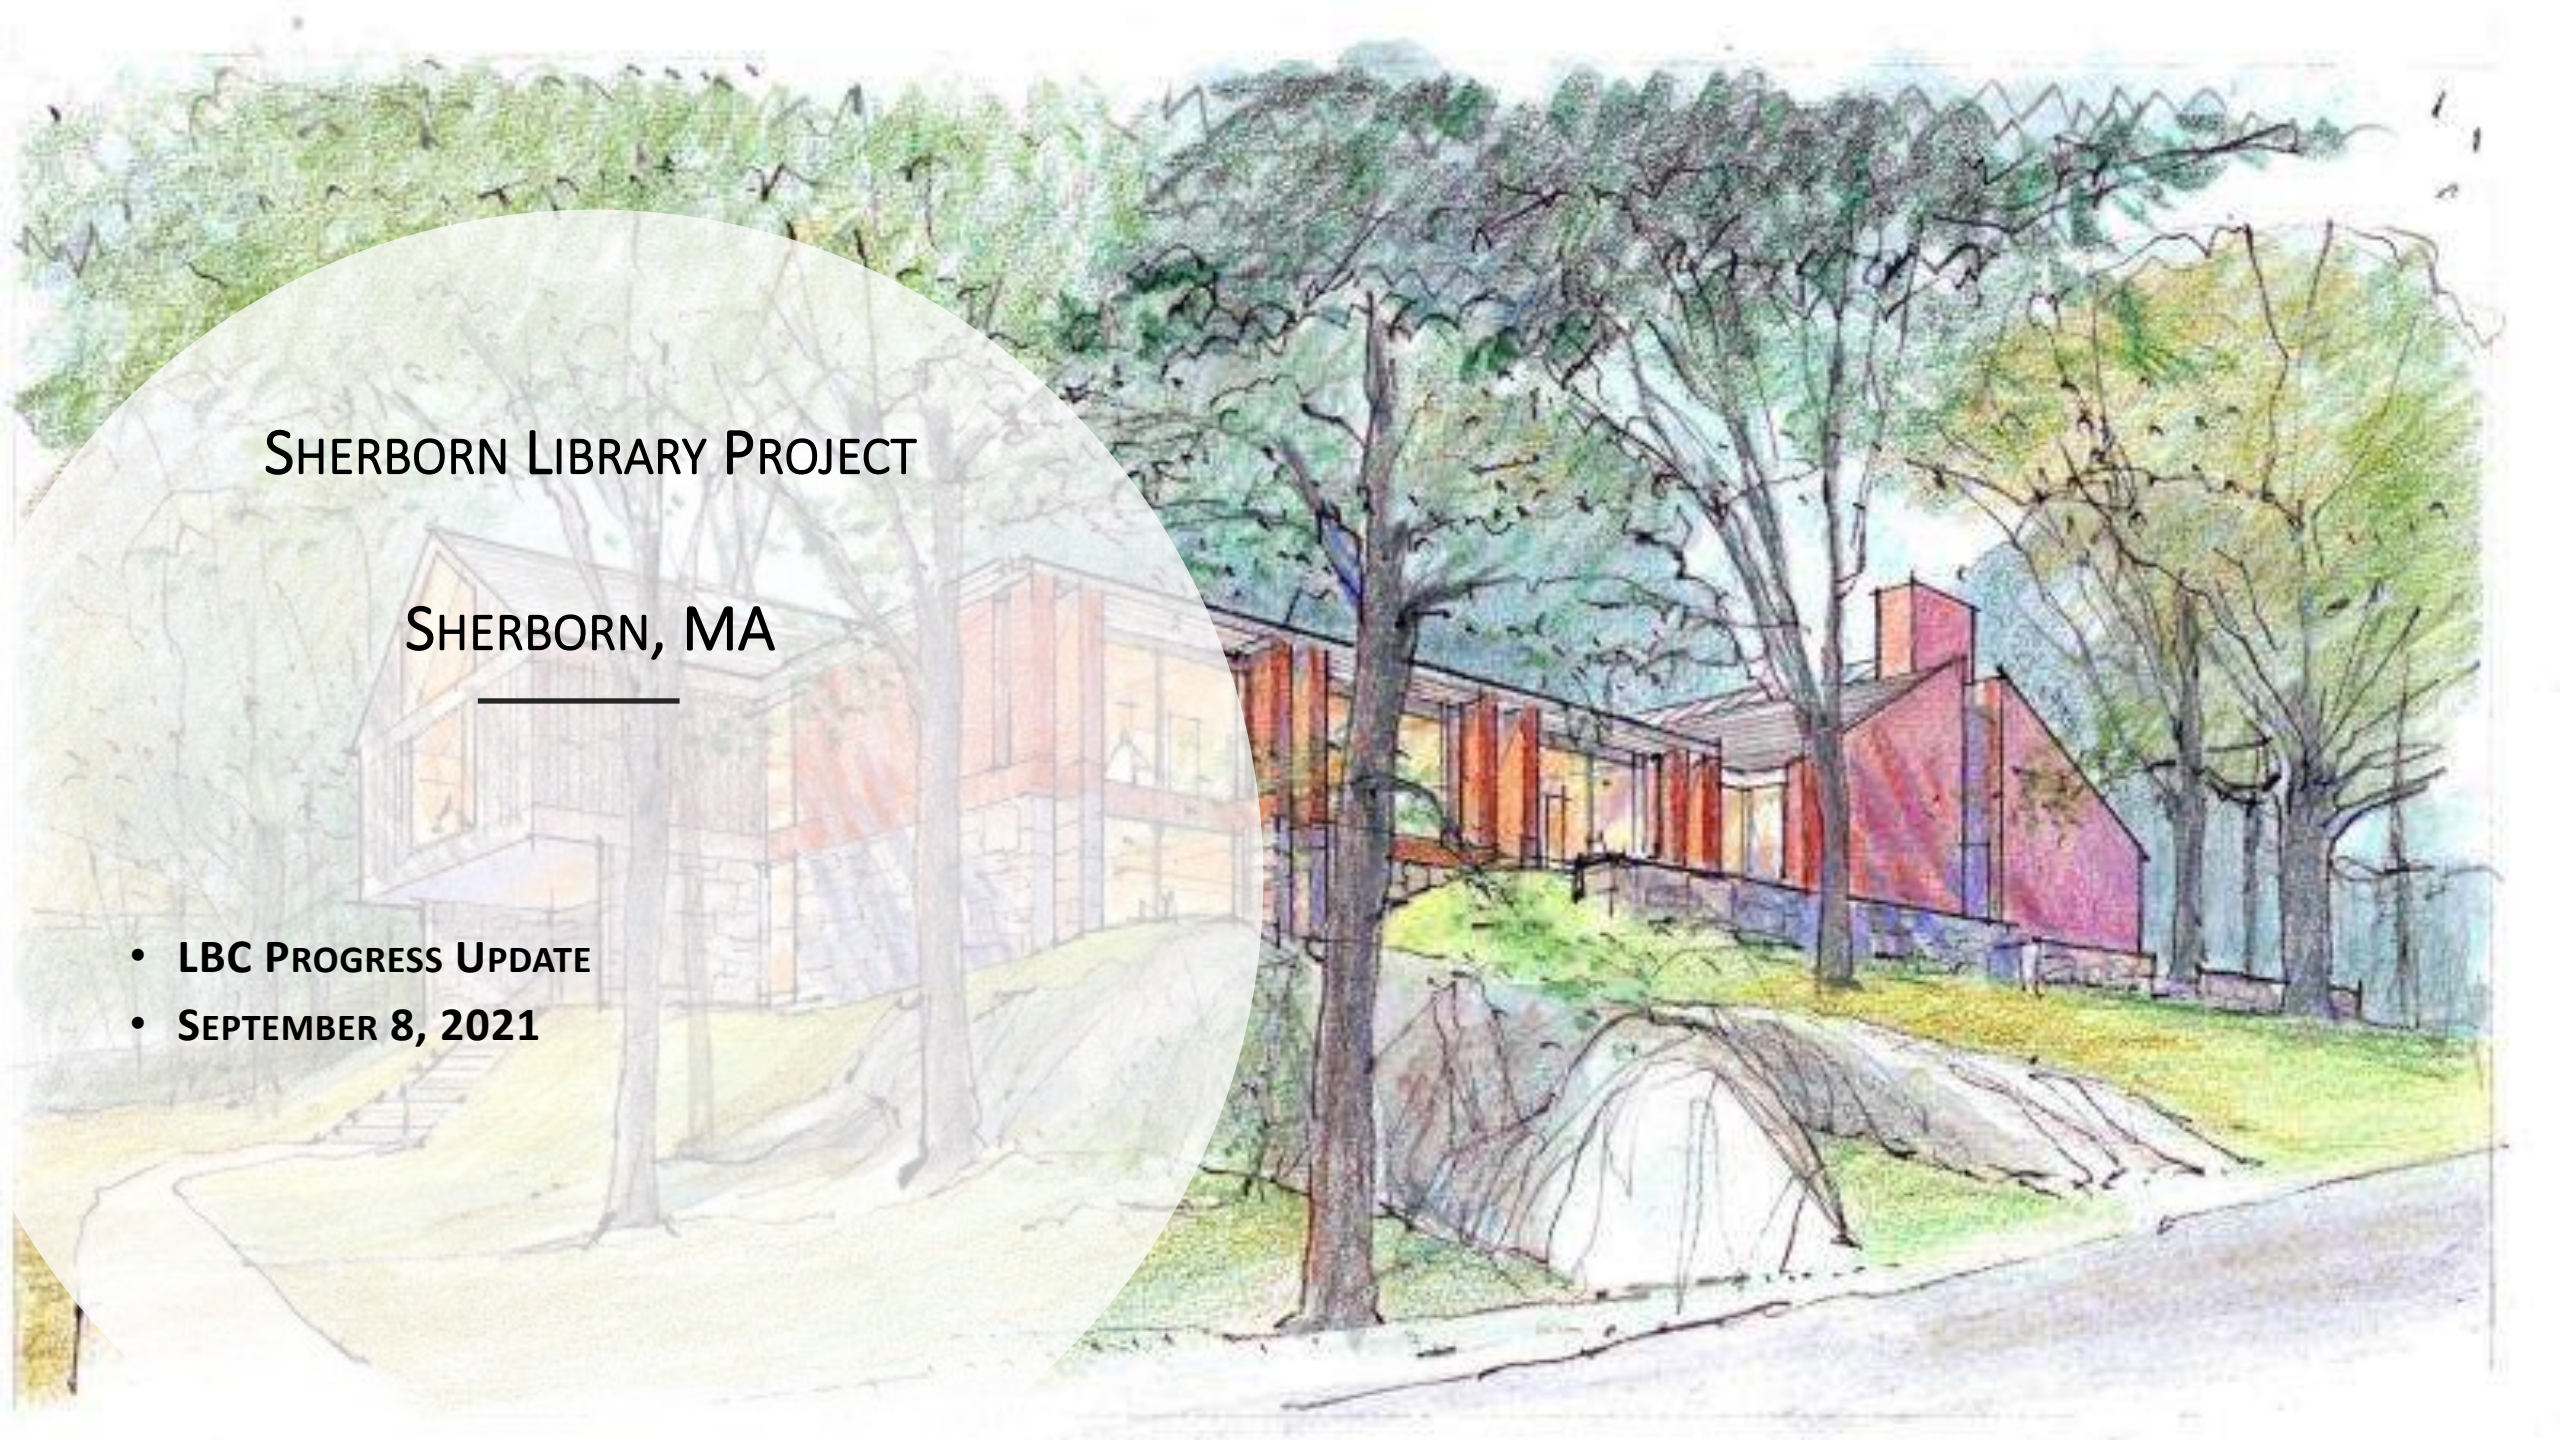

Site Utility Division

M-V
ELECTRICAL
Contractors, Inc.
508-995-3815

NO SMOKING
FIRE
BEACON
LIQUID NAILS
PROJECTS

EXIT

EXIT

SHERBORN LIBRARY PROJECT| SHERBORN MA

3 Week Look Ahead Schedule

PROJECT: SHERBORN LIBRARY PROJECT
PRINCIPAL: FIVE STAR BUILDING CORP
OBLIGEE: TOWN OF SHERBORN
DATE: 9/6/21

			Week #1							Week #2							Week #3							Comments
			M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	
Item #	Item / Task	Sub	9/6	9/7	9/8	9/9	9/10	9/11	9/12	9/13	9/14	9/15	9/16	9/17	9/18	9/19	9/20	9/21	9/22	9/23	9/24	9/25	9/26	
1	BAA Jobsite Review	BAA																						
2	BAA Review of Door Issues	BAA																						need follow-up direction- RFI 380
3	BAA Discovery of Existing conditions	BAA																						BAA response
4	Water Test Windows	Owner																						TBD
5	FTR Install	Snowden																						install pending Window testing
6	10 Day Notification	SMS																						New Notification w/ new workplar
7	Abatement	SMS																						
8	Misc. Interior Carpentry/Doors/Hardware - Change Order Work	Five Star																						pending approval of CRs & RFI 380
9	Modify copper flashing at chimney/skylight	Silktown																						pending Silktown confirmation/weather
10	Water Test Skylight	Owner																						to be scheduled while lift is on-site
11	Remaining Exterior Fixtures/UG wiring repair	MV																						
12	LED lights in railings	L&L																						Waiting on material
13	Owner's IT Work	Owner/SCS																						
14	Form & Pour Colored Concrete at Upper Walkway	ERA																						
15	Tie to existing walkway at Sanger St	ERA																						BCG to send CR
16	Raise Structures to final pave height	ERA																						
17	Survey Structures	GLM																						
18	Final Pave	ERA																						Follows walkway pour & Structures
19	Pump and Vaccum Septic System	Five Star																						
